



**JANUARY 9, 2026**

# **WEEKLY REPORT**

To: Kyle City Council  
From: City Manager Bryan Langley

# Table of Contents



**3**

**Executive Summary**

**4**

**Council Schedule**

**5**

**Council Requests**

**6**

**Board Vacancies**

**7**

**Infrastructure and Project Updates**

**13**

**Programs and Services Updates**

**16**

**Development Updates**

**17**

**Welcome to Team Kyle**

**18**

**Upcoming Events and Programs**

# Executive Summary

**Pedestrian safety improvements along Philomena Drive near IDEA Kyle School are nearing completion, with rapid flashing beacons expected to be operational by January 14.**

The City of Kyle continued steady progress on major infrastructure projects this week, with active work underway on water, wastewater, and roadway improvements. Electrical and mechanical installations advanced at Well Site #4 and the FM 1626 Ground Storage Tank and Pump Station, while water and wastewater line installation continued along Schlemmer Road. Work at CR 158 also progressed, with pipe supports and electrical conduit installation ongoing inside the elevated storage tank.

Wastewater projects remained active across the city. Crews continued installing pipe at the Plum Creek Golf Course sewer project, with testing confirming system integrity despite slower excavation caused by rock conditions. At Center Street Village, utility coordination is nearing completion, positioning the project to resume wastewater installation later this month. Early construction activities also continued at the Wastewater Treatment Plant, including excavation, materials testing, and reinforcing steel inspections.

Several mobility and safety projects reached key milestones. The Goforth Road Culvert Rehabilitation Project is complete and awaiting final walkthrough, while the Sanders speed table is curing and expected to reopen in mid-January. Pedestrian safety improvements along Philomena Drive near IDEA Kyle School continued, with rectangular rapid flashing beacons expected to be operational by January 14.

Construction, design, and community-focused projects also advanced. Multiple 2022 Road Bond corridors continued through construction and final design, while early site work began at the Gregg-Clarke All-Wheels Skatepark and building upgrades progressed at the Kyle Community Center. Library renovations remain on schedule, with staff completing operational improvements during the closure, and community engagement remained strong through park planning efforts, programs, and public input initiatives.

# Council Schedule

---

## **Tuesday, January 13**

Council Special Meeting at 5:30 p.m.

---

## **Tuesday, January 20**

Council Special Meeting at TBD

Council Regular Meeting at 7 p.m.

---

## **Tuesday, February 3**

Council Special Meeting at TBD

Council Regular Meeting at 7 p.m.

All meetings will be held at Kyle City Hall Council Chambers,  
100 W. Center St., unless otherwise noted.

All meetings conducted in the council chambers will be  
available via live stream on Kyle10.



# Council Requests

Item	Date	Request	Status
1	6/7/25	AMI Conversion Dashboard	Assigned to Mike Murphy; February 17, 2026
2	6/7/25	Tour of reuse facilities	Assigned to Mike Murphy; March 2026
3	6/17/25	Evaluate naming process for City facilities	Assigned to David Lopez; January 20, 2026
4	7/16/25	Develop a broad data policy; create a specific policy for this program if grant is awarded	Assigned to Jesse Elizondo; Presentation overview was provided 10/21/25; expect a contract to come forward Spring 2026
5	10/8/25	Provide options for proposed Kyle Public Library policy amendments	Assigned to Leslie Scott; January 20, 2026
6	12/2/25	Kohlers Bridge updated options for illumination and aesthetics	Assigned to Mike Trimble; Spring 2026
7	12/2/25	Bring back options to improve traffic at 1500 Dacy	Assigned to Mike Trimble; Spring 2026
8	12/2/25	Kyle Housing Assessment Report	Assigned to Rosie Truelove; Spring 2026
9	12/16/25	Anti-displacement Strategy	Assigned to Rosie Truelove; Spring 2026
10	1/6/26	Establish a Council Compensation Committee	Assigned to Aimee Alcorn-Reed; February 3, 2026
11	1/6/26	Evaluate the Council Expense Policy and eliminate Council credit cards	Assigned to Joshua Chronley; February 3, 2026
12	1/6/26	Develop a policy to require the posting of all credit card expenses, associated receipts, and other supporting information to the City's website	Assigned to Joshua Chronley; February 3, 2026

# Board Vacancies

Want to help shape the future of Kyle? The City is currently accepting applications for several open board positions. If you're a resident with a passion for public service and meet the qualifications, we encourage you to apply and get involved in your local government. Applications are accepted at [cityofkyle.gov/bc](http://cityofkyle.gov/bc) - Click Apply

---

## Arts and Cultural Board

Seat 2 - Artist Community Representative

Seat 4 - Artist Community Representative

Qualifications: <https://ecode360.com/45532165#45532168>

---

## Board of Adjustment

Alternate No. 1

Qualifications: <https://ecode360.com/45582416#45582433>

---

## Economic Development and Tourism Board

Seat 2 – Resident or Non-Resident Exec-level Rep of a Major Employer within Kyle city limits

Seat 5 - Resident/Owner of a Small Business (10 - 100 Employees) within Kyle city limits

Qualifications: <https://ecode360.com/45532149#45532153>

---

## Library Board

Seat 2

Seat 4

Qualifications: <https://ecode360.com/45532060#45532076>

---

## Planning and Zoning Commission

Seat 7

Qualifications: <https://ecode360.com/45532102#45532104>

---

## Train Depot Board

Seat 6

Qualifications: <https://ecode360.com/45532131>

# Infrastructure and Project Updates

## Schlemmer & Porter Wastewater Improvements Phase 3

Staff Contact: Mike Murphy

The contractor continues installing water and wastewater lines along Schlemmer Road and remains on schedule.



## FM 1626 Ground Storage Tank and Pump Station

Staff Contact: Mike Murphy

Crews are installing pump valving, chlorine lines, and structural components inside the pump building. Work continues on masonry, steel framing, and column installation as the facility progresses toward the next construction phase.



## Well Site #4 (La Verde)

Staff Contact: Mike Murphy

Electrical work is underway, with crews pulling wire for lighting and power connections across the site. This work supports continued progress on the pump station and related infrastructure.



## CR 158 Elevated & Ground Storage Tank

Staff Contact: Mike Murphy

Crews continue installing pipe supports and electrical conduit within the elevated storage tank. The steel tank crew is scheduled to return the week of January 12 to resume work.







### Plum Creek Golf Course Sewer Line

Staff Contact: Mike Murphy

Pipe installation continued last week, though excavation has been slowed by challenging rock conditions. Crews also tested a section of the 30-inch wastewater line to confirm system integrity and will continue testing manholes and installing pipe as work progresses.



### Center Street Village Wastewater Improvement

Staff Contact: Mike Murphy

AT&T anticipates completing fiber line adjustments by January 9. Once this work is finished, the contractor will remobilize and resume wastewater pipe installation later this month.



### Wastewater Treatment Plant Early Works Package

Staff Contact: Mike Murphy

Excavation and materials testing continue for major treatment structures, including aeration basins and clarifiers. Reinforcing steel for the rapid mix basins has been inspected and approved, and submittals remain under review as early construction activities proceed.



### Sanders Speed Table

Staff Contact: Mike Trimble

Concrete for the Sanders speed table is curing as planned. The roadway is expected to reopen by midday on January 16, 2026.



### Philomena Drive Pedestrian Accessibility and Safety Improvements

Staff Contact: Mike Trimble

Crews are installing curb ramps, crosswalk markings, and rectangular rapid flashing beacons along Philomena Drive in front of IDEA Kyle School. This mid-block crossing is intended to improve pedestrian safety for students. The beacons are expected to be operational by January 14, 2026.



### Goforth Road Culvert Rehabilitation Project

Staff Contact: Mike Trimble

The Goforth Road Culvert Rehabilitation Project is complete following interim maintenance at two culvert sites identified with structural and hydraulic deficiencies during a prior engineering assessment. This work addresses immediate public safety needs. A final walkthrough is scheduled for January 9, 2026, to confirm all work has been completed in accordance with project requirements.



### Gregg-Clarke All-Wheels Skatepark

Staff Contact: David Lopez

The contractor has begun mobilizing equipment and initiating earthwork activities. These efforts mark the early stages of construction as site preparation continues.



### Kyle Community Center

Staff Contact: David Lopez

Building upgrades at the Kyle Community Center continue. Underslab inspections have been completed, and crews are proceeding with backfill activities as the project advances.



### Open House: Steeplechase and Lake Kyle Parks

Staff Contact: David Lopez

The Kyle Parks & Recreation Department will host an Open House on Tuesday, January 13th from 6 P.M. – 8 P.M. to gather community input on early concept plans for improvements at Steeplechase Park and Lake Kyle Park. Residents are invited to drop in, review preliminary ideas, and share feedback with staff and project consultants. The Open House will be held at the Kyle Public Works Building located at 520 FM 150.



### New Park Benches Installed

Staff Contact: David Lopez

New benches have been installed at the Waterleaf and Steeplechase playground areas. Designed with comfort, durability, and aesthetics in mind, these upgrades enhance the visitor experience while setting a consistent standard for high-quality amenities across the park system, one that will continue to be rolled out in parks citywide.







# 2022 Road Bonds Update

Staff Contact: Mike Trimble

[KyleRoadBonds.com](http://KyleRoadBonds.com)

## Kohlers to Seton

### Stage: Construction

Right-of-way and easements are confirmed as clear, allowing construction to proceed. Ongoing work includes bridge pier installation at Kohler & Seton intersection, embankment work at the proposed Kohlers Crossing/Bebbee Rd roundabout, and existing utility coordination and relocation work. Upcoming work will consist of Kohler embankment in front of Carroway Development and IH-35 frontage roadway Kohlers Crossing right turn-lane construction.



### Kohlers to Seton (IH-35 at Kohlers Crossing)

#### Stage: Early Design

The schematic design remains at 90% completion. The draft Intersection Control Evaluation review comments were received from TxDOT on December 15, 2025, indicating that the previously proposed innovative intersection option is not supported. The design team is currently identifying an alternative intersection configuration to integrate into the schematic. Completion of the 100% schematic submittal will depend on final review and TxDOT response, with a tentative target of January 30, 2026.



## Bebbee Rd

### Bebbee Road (West)

#### Stage: Construction

Construction continues in coordination with the Kohlers to Seton project. Ongoing work includes roadway embankment construction and stormwater drainage culvert installation along the future Bebbie Road alignment from Republic Drive to the planned Kohlers Crossing/Bebbee Road roundabout. Crews are also installing stormwater systems, excavating the detention pond, foundation work on retaining walls, and wastewater bore under Bebbie. Upcoming activities include continued embankment and drainage work as well as additional roadway base preparation.



### Bebbee Road (East)

#### Stage: Final Design

The 100% PS&E (Plans, Specifications, and Estimates) were received on December 19, 2025, and are under City review through January 10, 2026.



# 2022 Road Bonds Update (Continued)



### Heritage Oak Tree Move Update

Old Stagecoach Road repairs are complete, and road reopened following the relocation of the tree.

### Old Stagecoach Rd

#### Old Stagecoach Road North

##### Stage: Final Design

The 90% PS&E comment-resolution meeting was completed on December 15, 2025. All initial right-of-way offers have been issued, and the project is advancing toward the 100% PS&E milestone, which is expected on February 13, 2026.

#### Old Stagecoach Road

##### Stage: Final Design

The 95% PS&E submittal is expected on January 9, 2026. The right-of-way is confirmed as clear.

#### Center Street (West Segment)

##### Stage: Final Design

The revised 100% PS&E documents were submitted on December 22, 2025. Bid advertising began on January 5, 2026. Utility coordination continues, with AT&T relocations expected to proceed.

### Center Street

#### Center Street (East Segment)

##### Stage: Final Design

Design for the on-system portion of Center Street (FM 150) is at 50% completion. The 60% PS&E submittal is expected on February 24, 2026, and the TxDOT Review and Technical Coordination meeting is scheduled for March 11, 2026.

### Bunton Creek Rd

#### Stage: Final Design

The project is at 95% design completion. The draft project manual was approved on December 26, 2025, and bid advertising is scheduled to begin on February 9, 2026. Right-of-way offers have been issued and are currently under negotiation.

### Windy Hill Rd

#### Stage: Construction Bidding

Bid advertising for construction contractors began on December 8, 2025. During this period, the project was publicly advertised to solicit competitive bids from qualified contractors. The bid opening is scheduled for January 22, 2026, at which time all submitted bids will be received and reviewed for responsiveness and compliance prior to a recommendation for award.

### Kyle Pkwy/Lehman Ext.

#### Stage: Final Design

Design is at 95% completion. A cost-reduction design resubmittal was received on December 21, 2025, and is under review through January 9, 2026.

### Marketplace Ave

#### Stage: Substantial Completion

Construction is approximately 85% complete. Final inspections are pending, and Vybe Trail punch-list items are being addressed.

See all the project details and updates at [KyleRoadBonds.com](https://kyleroadbonds.com)

# Programs and Service Updates

## Community Bird Walks

Staff Contact: David Lopez


Parks and Recreation recently hosted guided bird walks led by Master Naturalist Doray Lendacky, focusing on local wildlife. The Bunton Wildflower Loop had 8 attendees, while the Lake Kyle Park tour for National Bird Day attracted 20 participants, showing growing interest in nature programs. A third bird walk is set for January 24th, open to the community, with more details at [kylerec.recdesk.com](http://kylerec.recdesk.com).



## Feral Hog Update

Staff Contact: David Lopez

In mid-December, Parks and Recreation staff resumed trapping feral hogs at Lake Kensington Park and Waterleaf Park, capturing five hogs that were taken to a USDA facility. They continue to monitor and adjust strategies to protect park resources and visitor safety. Since the program began in 2025, 63 hogs have been removed from parks.



## 2026 Polar Bear Splash

Staff Contact: David Lopez

The annual Polar Bear Splash took place on January 1, 2026, at the James Adkins Pool, coinciding with For the Love of Go's Resolution Run 5K. The event attracted over 175 participants and numerous spectators, creating an energetic atmosphere. Dutch Bros enhanced the experience by providing complimentary coffee, adding warmth to the cold-weather celebration.





## Holiday Season Comes to a Close

Staff Contact: David Lopez

The City of Kyle Parks and Recreation Department concluded its 25 Days of Christmas, a month-long celebration offering diverse holiday programming for residents. Highlights included Grinch on the Green, the Winter Wonderland Dance for All Abilities, Santa's Arrival, Santa Rides in Kyle, weekly visits with Santa, karaoke nights, local food and craft vendors, and live performances by community bands. Families and neighbors enjoyed strolling through holiday lights and seasonal activities that supported local businesses and performers.

A highlight of the season was the debut of new, permanent, and dark sky friendly LED lighting on the decommissioned downtown water tower. Holiday light displays were available at three locations, Mary Kyle Hartson, La Verde, and Lake Kyle Park, creating spaces across the city to celebrate the season.

The 25 Days of Christmas remains a beloved tradition, with plans to welcome the community back again next year.





# Kyle Public Library Renovation Update

Staff Contact: Leslie Scott

Library renovation work remains on schedule, with approximately two-thirds of the facility now painted and half of the new carpet installed. Carpet replacement in program and meeting rooms is complete, and remaining areas will be addressed in phases as materials are moved to allow work to continue without delay.

While the library is closed, staff are focused on internal projects that support daily operations and future service delivery. Activities this week include City of Kyle trainings, reorganizing and relabeling adult fiction collections, processing new materials, cleaning up records, and helping develop standard operating procedures. Staff are also expanding familiarity with online resources to better support patrons when the library reopens.

Overall renovation progress continues as planned, with painting and flooring work advancing steadily throughout the building.



## Heroes Memorial Park Restaurant Survey

Staff Contact: Victoria Vargas



The City of Kyle launched a public survey this week to gather resident input on a potential restaurant at the parkside site adjacent to Heroes Memorial Park within the Brick and Mortar District/TIRZ #2. Within the first 24 hours, the survey received 1,095 responses, reflecting strong community interest and engagement. The survey remains open through January 23, 2026 at [surveymonkey.com/r/heroesrestaurant](https://surveymonkey.com/r/heroesrestaurant). Final results will be shared with City Council to help inform next steps.

# Welcome to Team Kyle!

The City of Kyle has recently welcomed new employees to our team! If you come across any of our new staff members, please take a moment to offer them a warm welcome.



**Lane Delling**

Police Officer, KPD  
Joined Team Kyle on January 4



**Ryan Rhodes**

Police Officer, KPD  
Joined Team Kyle on January 4



**Pablo Gonzalez**

Project Manager, TPW  
Joined Team Kyle on January 4



**Matt Cullen**

Project Manager, TPW  
Joined Team Kyle on January 4




**Naomi Trevino**

Project Coordinator, TPW  
Joined Team Kyle on January 4



**Alessa Bailey**

Project Coordinator, TPW  
Joined Team Kyle on January 4

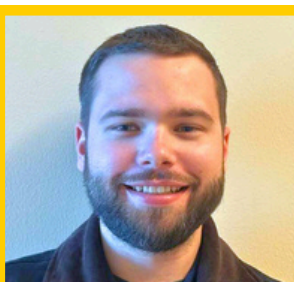

**Korbin Weese**

Code Enforcement Officer, Dev Services  
Joined Team Kyle on January 4



# Upcoming Events and Programs



## Parks Open House

Tuesday, Jan 13 from 6 - 8 p.m.  
Kyle Public Works Building  
[More Info](#)



## Senior Bingo

Thursday, Jan 15 from 10:30 a.m. - Noon  
Krug Activity Center  
[More Info](#)



## KASZ Chair Volleyball

Friday, Jan 16 at 11 a.m.  
Krug Activity Center  
[More Info](#)



## Future Careers Expo

Wednesday, Jan 21 at 10 a.m.  
San Marcos Activity Center  
[More Info](#)



## Trail Clean-Up


Thursday, Jan 22 at 8 a.m.  
Steeplechase Park  
[More Info](#)



## Bird Walk

Saturday, Jan 24 from 8 - 10 a.m.  
Linebarger Lake  
[More Info](#)





## **Stay Connected to Kyle!**

Stay up to date on everything that is happening in the city! Sign up to receive the [weekly e-newsletter](#), read up on the latest Kyle News at [KyleTXNews.com](http://KyleTXNews.com) and follow us on social media.



**Kyle Communications Department**  
[CommunicationsDept@CityofKyle.com](mailto:CommunicationsDept@CityofKyle.com)
